



BLUEPRINT TECH · SHOP FLOOR INTELLIGENCE

Integrated Kaizen & Shop Floor Control (SFC) Intelligence Platform

Data Generation Architecture, Executive Dashboards & Project Implementation Roadmap

TARGET AUDIENCE

Plant Head · Operations Leadership · Minifactory Management

PRESENTER


😊 [Your Name / Title]

TIMELINE WINDOW

August 10, 2026 – September 28, 2026

DECK VERSION

Executive Briefing - v1.0





Bridging Physical Shopfloor Activities with Real-Time Management Dashboards

Turning operator-level telemetry into board-level decisions.

CORE VALUE PROPOSITION

The platform closes the loop between every physical shopfloor event and the executive dashboard. Every kaizen submitted, every red flag raised, every 5S audit scored, and every safety near-miss logged is captured at source with photographic evidence and timestamped telemetry — then routed through integrated SFC modules into one analytics layer the plant leadership team can act on in hours, not weeks.

7

WEEKS TO FULL GO-LIVE

6

INTEGRATED SFC MODULES

5

EXECUTIVE DASHBOARDS



01

From Paper to Digital Telemetry

Every operator idea, machine breakdown, safety near-miss, and 5S audit is captured digitally at source with photos and timestamps.



02

Integrated Data Pipeline

Kaizen is directly coupled with the Shop Floor Control (SFC) modules — Red Flags, 5S, Safety, PPSR, Open Impact Actions.



03

Automated Executive Dashboards

Real-time visibility into Kaizen density per employee, validated INR cost savings, line-wise defect trends, and 5M compliance.



04

Proven 7-Week Delivery

Phased project roadmap guaranteeing full production handover and hypercare by September 28, 2026.



Granular Shopfloor Data Generation Across All Connected Modules


Six SFC modules → six structured data inventories, all feeding one analytics layer.



Closed-Loop Data Interactivity Between Shopfloor Modules

How module data cross-pollinates — every flag, audit, and incident automatically spawns the right downstream Kaizen action.

◎ SFC MODULE RAIL

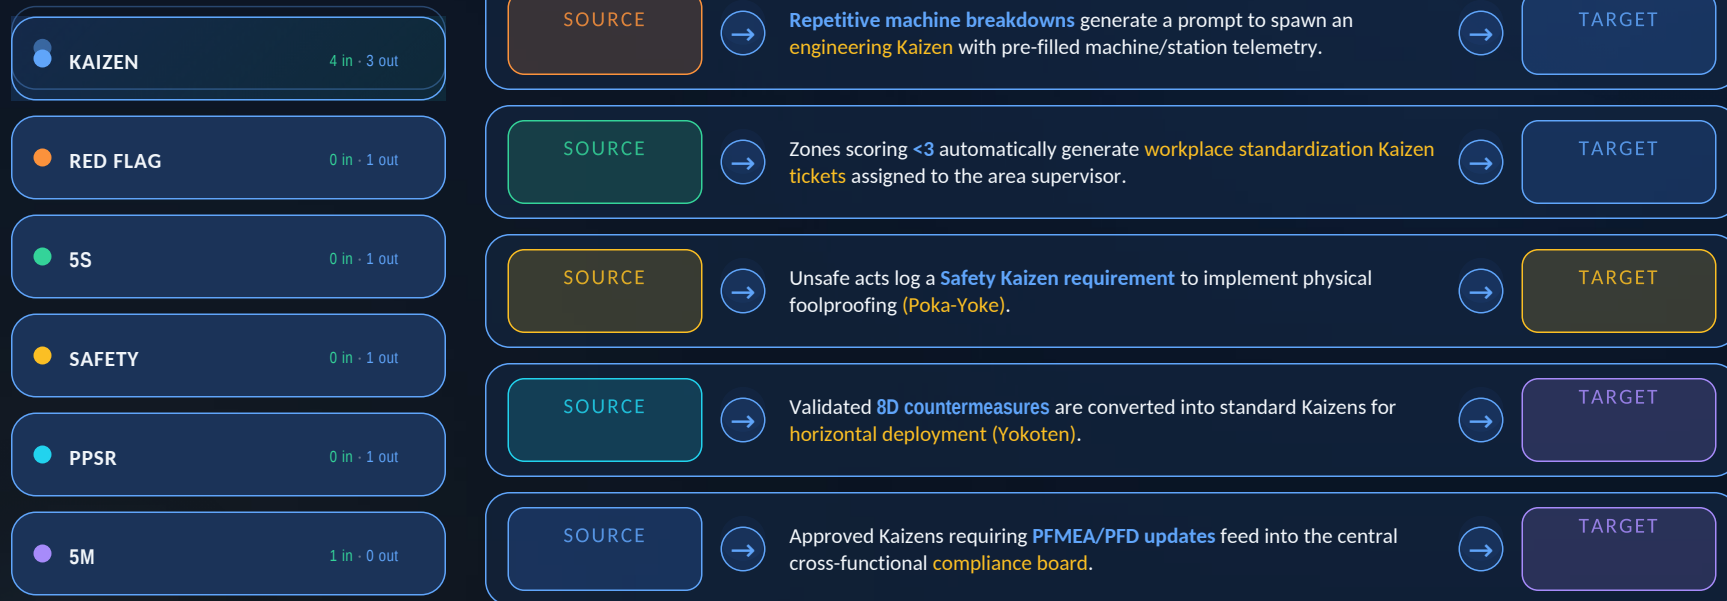

🔄 CLOSED-LOOP INTEGRATION • ALL 5 FLOWS ACTIVE • ZERO MANUAL HANDOFF

SYNC LATENCY < 200ms • LAST RUN 14:38:02 IST

Executive Analytics & Financial Impact Board

High-level plant performance & financial trajectory.

YEAR: 2025

MONTH: ALL

TYPE: KAIZEN

STATUS: OPEN



EXPORT PDF

TOTAL KAIZENS (2025 YTD)

409+

↑ +7.5% YoY vs FY24 (380)

COST SAVED (INR ₹)

₹8.87L

↑ +1.0% vs FY24 validated by finance


KAIZEN INTENSITY (PER EMP)

1.37


↑ from 1.13 (FY21) plant-wide coverage

YOY KAIZEN IMPLEMENTATION GROWTH

IMPLEMENTED KAIZENS / YEAR

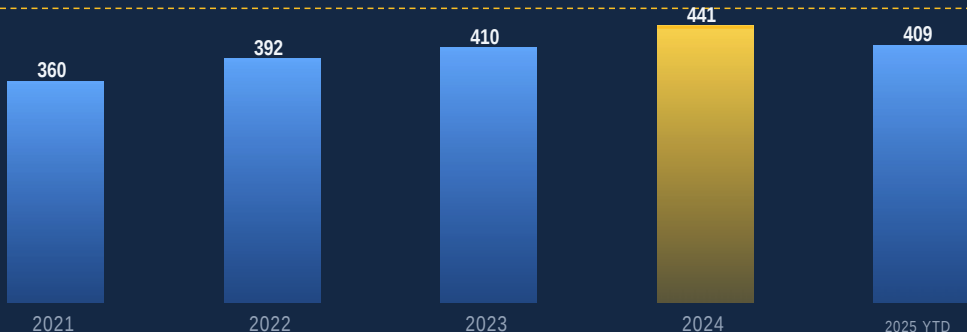

DEPARTMENTAL SAVINGS SHARE

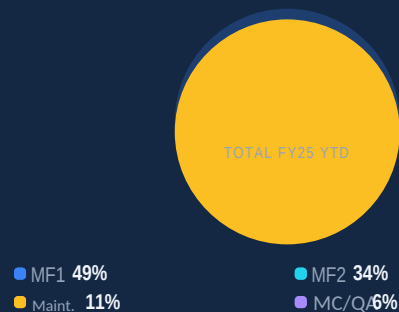

Plant-Wide SFC Global Command Center

Unified operational health & multi-module plant radar.

TOTAL LOGGED KAIZENS

1,847



ACTIVE RED FLAGS

23



OVERALL 5S SCORE

87.4%



OPEN SAFETY ITEMS

6




LIVE RED FLAG STATUS BY DEPARTMENT

Closed In-Progress Open

MF1	45	8	4	57
MF2	38	6	3	47
MF3	41	9	5	55
MC	28	4	2	34
MAINT	22	5	6	33
QA	18	3	3	24

5S PLANT-WIDE RADAR

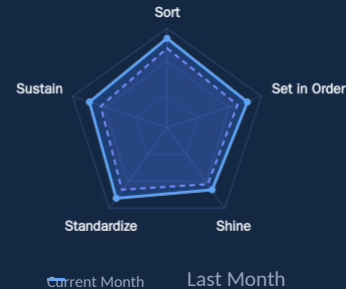

CROSS-MODULE SLA ALERT FEED

LIVE · REFRESH 30s

- KAIZEN** DEL-4.2 evaluation overdue · MF3 Line 7 2d late
- SAFETY** Containment action pending · MF1 Robot Cell 3 6h late
- PFMEA** Update not started · MC Spindle Station 1d late

QUICK LAUNCHPAD



KAIZ



RED



5S



SAF



PPSR



5M

Minifactory & Line-Level Kaizen Management Board

IDEA VS KAIZEN CONVERSION




Ideas
Pending conversion **314**

Kaizens
Formally logged **1,533**

Total submissions · **1,847**

STATUS PIPELINE DISTRIBUTION

N = 1,847



MONTH-ON-MONTH VOLUME VELOCITY


JAN - DEC 2024



BENEFIT VECTOR MIX (P-Q-C-D-S-M)



PRIMARY BENEFIT VECTOR - 6-AXIS CLASSIFICATION



MINIFACTORY VOLUME BREAKDOWN

MF1 612

MF2 487

MF3 421

MC 168

MAINT 102

QA 84


NCM 53

PPSR & Quality Engineering Deep-Dive Board


Root-cause analytics, defect trends & financial savings per unit.

DEFECT TREND & FTQ BEFORE/AFTER


FTQ: 22PP



ISHIKAWA (FISHBONE) & 5-WHY MATRIX



PSQ ELIMINATION TREE VISUALIZER



STANDARDIZED FINANCIAL MODEL PER REJECTION SET

METRIC	VALUE
Rejection Rate Before	240 PPM
Rejection Rate After	35 PPM
Cost per Rejection (₹)	₹420
Monthly Volume (units)	85,000

STANDARDIZATION & READ-ACROSS TRACKER

Machine A
Deployed

Machine B
Deployed

Machine C
In Progress

Machine D
Pending

SISTER-MACHINE DEPLOYMENT · 2 / 4 COMPLETE

CFT Monthly Awards & Employee Participation

Leaderboard

EMPLOYEE KAIZEN SUBMISSION LEADERBOARD

CYCLE · OCT 2024

RANK	EMPLOYEE NAME	DEPT	SUB.	APP.	SAVINGS (₹)
1	Ramesh K	MF1	47	41	₹1.84L
2	Suresh M	MF2	39	35	₹1.42L
3	Anita P	MF3	36	32	₹1.18L
4	Vikram S	MAINT	28	24	₹0.94L
5	Deepak R	MC	24	21	₹0.78L

MINIFACTORY KAIZEN DENSITY METER

KAIZENS / 100 OPERATORS

MF1

1.62

MF2

1.41

MF3

1.28

MC

1.14

MAINT

0.98

QA

0.87

PLANT AVE

1.37

TOP PERFORMER · MF1

CFT EVALUATION PORTAL

JA

Judge A

E8

I9

V7

24/30

CFT CHAIR

SK

Judge B

E7

I8

V9

24/30

PROCESS HEAD

VOTING OPEN · 2/3 SUBMITTED

E=EFFECT · I=IMPACT · V=INNOVATION

MONTHLY BEST KAIZEN SHOWCASE

Ramesh K

Auto Gauging Fixture

1

Suresh M

Quick Changeover Jig

2

Anita P

Poka-Yoke Sensor

3

TV DISPLAY READY

DIGITAL CERTIFICATE & A3 PDF EXPORT

CERTIFICATE OF RECOGNITION

CFT Monthly Kaizen Award · OCT 2024

Ramesh K

for outstanding contribution · MF1 Line 4

SIGNED · CFT CHAIR

ID · KZ-2024-1847

1-CLICK · AUTO-FILLED

DASHBOARD 05 · CFT AWARDS & LEADERBOARD

09 / 15

Open Impact Assessment & 5M / Yokoten Compliance



6-Phase End-to-End Delivery Timeline (Aug 10, 2026 – Sep 28, 2026)

TOTAL DURATION

7 Weeks

PHASES

6

GATE REVIEWS

6

GO-LIVE DATE

Sep 28, 2026**1 Discovery Workshop**

Aug 10 – Aug 17 · 7 days

2 System Analysis & BRD/FRS

Aug 18 – Aug 24 · 7 days

3 Architecture & DB Design

Aug 25 – Aug 31 · 7 days

4 Core Development & Internal Testing

Sep 01 – Sep 18 · 18 days · LONGEST PHASE

5 UAT & Bug Fixing

Sep 19 – Sep 25 · 7 days

6 Deployment & Go-Live

Sep 26 – Sep 28

AUG 10

AUG 17

AUG 24

AUG 31

SEP 07

SEP 14

SEP 18

SEP 25

SEP 28

**TOTAL DURATION: 7 WEEKS TO FULL PRODUCTION GO-LIVE · AUG 10 → SEP 28, 2026**



Requirements, Process Mapping & Architecture Milestones

Phase 1 (Aug 10-17) · Phase 2 (Aug 18-24) · Phase 3 (Aug 25-31)

PHA	PHASE NAME	START	END	DEL. ID	KEY DELIVERABLE / MILESTONE	DETAILED APPROACH & METHODOLOGY	RESPONSIBILITY
1	Requirement Gathering & Discovery	Aug 10, 2026	Aug 11, 2026	DEL-1.1	Project Charter & Stakeholder Alignment Matrix	Conduct kickoff meeting, establish communication protocols, define governance framework, and map key business/technical stakeholders.	Ganesh, Sachin K
1	Requirement Gathering & Discovery	Aug 11, 2026	Aug 13, 2026	DEL-1.2	Process Mapping (As-Is vs. To-Be) & Scope Definition	Facilitate interactive workshops with Kaizen process owners to map current continuous improvement workflows, pain points, and target state.	All Minifactory Managers & Manoranjan B
1	Requirement Gathering & Discovery	Aug 14, 2026	Aug 16, 2026	DEL-1.3	User Personas & Discovery Synthesis Report	Classify user roles (Submitter, Reviewer, Approver, Executive) and synthesize functional capabilities, reporting needs, and integration touchpoints.	Sachin K
1	Requirement Gathering & Discovery	Aug 17, 2026	Aug 17, 2026	DEL-1.4	Phase 1 Gate Review & Discovery Sign-off	Formal review of discovery findings, high-level scope baseline, and authorization to proceed to detailed system analysis.	Sachin K
2	System Analysis & BRD/FRS Sign-off	Aug 18, 2026	Aug 20, 2026	DEL-2.1	Business Requirements Document (BRD)	Draft granular functional/non-functional requirements including Kaizen submission workflows, review hierarchies, scoring logic, and SLA triggers.	Om Deole
2	System Analysis & BRD/FRS Sign-off	Aug 20, 2026	Aug 22, 2026	DEL-2.2	Functional Requirement Specification (FRS) & UI Wireframes	Develop detailed UI wireframes, screen interaction flows, state transition diagrams, and mapping of automated notification rules.	Om Deole
2	System Analysis & BRD/FRS Sign-off	Aug 23, 2026	Aug 23, 2026	DEL-2.3	Requirements Traceability Matrix (RTM) & Data Rules	Establish end-to-end trace from business goals to functional items; document field-level data validation rules and approval hierarchy logic.	Sachin K
2	System Analysis & BRD/FRS Sign-off	Aug 24, 2026	Aug 24, 2026	DEL-2.4	Phase 2 Gate Review & Formal BRD/FRS Sign-off	Present BRD and FRS package for formal sign-off. Baseline functional scope prior to entering architectural and technical design.	Sachin K, All MF Managers & Manoranjan B
3	System Architecture & Database Design Sign-off	Aug 25, 2026	Aug 27, 2026	DEL-3.1	System Design Document (SDD) & Architecture Blueprint	Design multi-tier system architecture, component interaction models, API patterns, authentication models, and audit logging frameworks.	Swaraj
3	System Architecture & Database Design Sign-off	Aug 27, 2026	Aug 29, 2026	DEL-3.2	Database ER Schema & Data Dictionary	Construct ERD for Kaizen ideas, status progression, attachments, scoring metrics, and ROI tracking tables. Define indexing and constraints.	Swaraj
3	System Architecture & Database Design Sign-off	Aug 30, 2026	Aug 30, 2026	DEL-3.3	Security, Compliance & API Contract Specification	Define RBAC security matrices, data encryption standards, and REST API payload contracts for integration with corporate identity/ERP systems.	OM + Swaraj
3	System Architecture & Database Design Sign-off	Aug 31, 2026	Aug 31, 2026	DEL-3.4	Phase 3 Gate Review & Architecture Sign-off	Technical review and formal sign-off of SDD, schema, and security architecture before unlocking developer coding phase.	Sachin K, All MF Managers & Manoranjan B



Build Execution, Business Testing & Plant Handover Milestones

Phase 4 (Sep 01-18) · Phase 5 (Sep 19-25) · Phase 6 (Sep 26-28)

PHA	PHASE NAME	START	END	DEL. ID	KEY DELIVERABLE / MILESTONE	DETAILED APPROACH & METHODOLOGY	RESPONSIBILITY
4	Core Development & Internal Testing	Sep 01, 2026	Sep 07, 2026	DEL-4.1	Database Provisioning & Core Backend API Engine	Provision staging DB, implement ORM entities, write CRUD microservices, workflow state engines, and notification triggers.	Swaraj
4	Core Development & Internal Testing	Sep 06, 2026	Sep 12, 2026	DEL-4.2	Frontend UI Development & Design System Integration	Build responsive web interfaces for Kaizen submission forms, approval dashboards, status Kanban boards, and analytics widgets.	Om Deole
4	Core Development & Internal Testing	Sep 13, 2026	Sep 15, 2026	DEL-4.3	Automated Unit Testing & System Integration	Execute full API integration with frontend components; achieve >80% unit test coverage; validate notification engine and RBAC enforcement.	Om Deole
4	Core Development & Internal Testing	Sep 16, 2026	Sep 17, 2026	DEL-4.4	QA System Testing, Performance & Defect Remediation	Perform full functional QA cycles, security vulnerability scans, and load testing. Fix all Critical/High severity defects prior to UAT release.	Om Deole
4	Core Development & Internal Testing	Sep 18, 2026	Sep 18, 2026	DEL-4.5	Phase 4 Gate Review & Code Freeze / Readiness for UAT	Code freeze execution; review test execution reports and defect burn-down. Formal sign-off to release build to UAT environment.	Sachin K, All MF Managers & Manoranjan B
5	User Acceptance Testing (UAT) & Bug Fixing Sign-off	Sep 19, 2026	Sep 20, 2026	DEL-5.1	UAT Environment Deployment & Business Onboarding	Deploy code freeze build to UAT environment, load synthetic master data, conduct UAT orientation with business champions, and distribute test scripts.	OM + Swaraj
5	User Acceptance Testing (UAT) & Bug Fixing Sign-off	Sep 21, 2026	Sep 23, 2026	DEL-5.2	Business UAT Execution & Defect Triage	Business key users execute end-to-end business scenarios (idea submission, approval flow, tracking, ROI calculation); daily defect triage.	OM + Swaraj
5	User Acceptance Testing (UAT) & Bug Fixing Sign-off	Sep 23, 2026	Sep 24, 2026	DEL-5.3	UAT Bug Fixes, Patch Deployment & Re-test	Development team resolves logged UAT defects; deploy patch builds and verify resolution with business testers to reach zero blocker/critical issues.	OM + Swaraj
5	User Acceptance Testing (UAT) & Bug Fixing Sign-off	Sep 25, 2026	Sep 25, 2026	DEL-5.4	Phase 5 Gate Review & Formal UAT Sign-off	Review UAT sign-off matrix, outstanding minor issues register, and obtain formal business sign-off approving Production deployment.	Sachin K, All MF Managers & Manoranjan B
6	Production Deployment, Training & Hypercare Handover	Sep 26, 2026	Sep 26, 2026	DEL-6.1	Production Deployment & Cutover Execution	Execute production deployment runbook, run database migration scripts, perform smoke testing, and transition DNS/routing.	OM + Swaraj
6	Production Deployment, Training & Hypercare Handover	Sep 27, 2026	Sep 27, 2026	DEL-6.2	End-User Training, Admin Enablement & Documentation	Conduct role-based end-user training, deliver admin operating manuals, quick-reference guides, and knowledge base articles.	OM + Swaraj
6	Production Deployment, Training & Hypercare Handover	Sep 28, 2026	Sep 28, 2026	DEL-6.3	Hypercare Handover & Project Closure Sign-off	Transition system support to L2/L3 IT Operations team, activate initial hypercare support window, and execute formal project completion certificate.	OM + Swaraj

✓ PROJECT GO-LIVE · SEP 28, 2026 · HYPERCARE ACTIVATED

Strict Stakeholder Sign-Offs at Every Critical Checkpoint

Mandatory gate reviews — no phase advance without formal sign-off. Six governance gates ensure zero scope creep and full business accountability.

GOVERNANCE PRINCIPLE

No phase advances without a formal sign-off from the accountable stakeholders.

Gate 1 · Aug 17
Gate 2 · Aug 24
Gate 3 · Aug 31
Gate 4 · Sep 18
Gate 5 · Sep 25
Gate 6 · Sep 28

6 GATE REVIEWS

0 SCOPE CREEP TOLERANCE

100% STAKEHOLDER ACCOUNTABILITY

QUALITY GATES & GOVERNANCE





Measurable Business Returns from Integrated SFC Intelligence

Expected Returns and Strategic Business Action



Data Integrity

100% digital capture eliminates lost ideas and unverified savings claims. Every kaizen, red flag, and audit leaves a permanent auditable trail with photographic evidence.

100% DIGITAL CAPTURE



Cycle Time Reduction

Kaizen approval and review cycle cut from weeks to hours through automated workflow routing, SLA triggers, and one-click CFT evaluation.

Weeks → Hours



Financial Governance

Real-time visibility into annual cost savings (₹) by line and department, with validated ROI tracking and CFT-verified monetary impact reporting.

₹8.87L+ YTD FY25



Empowered Workforce

Real-time recognition via CFT awards and leaderboard visibility boosting operator engagement and sustaining a continuous improvement culture.

1.37 KAIZENS / OPERATOR



IMMEDIATE CALL TO ACTION

1

Formal sign-off on Phase 1 kickoff (DEL-1.1)

DUE: AUG 10, 2026

2

Mobilization of Minifactory Managers for Process Mapping workshops starting August 11, 2026

KICKOFF: AUG 11, 2026



Open Floor for Discussion

project@blueprint.tech

Schedule Follow-up

Request Full BRD
